Clients Name	:	**BRUHAT BENGALURU MAHANAGARA PALIKE**
Project Name	:	**EXECUTIVE ENGINEER YELAHANKA DIVISION**
Consultants	:	**Construction of Classrooms to Govt PU College and providing grill fencing and Other developmental Works to ISRO layout Park, Vishweshwaraiya park, Raj kumar Park, Sri Sailputra park Yelahanka Assembly Constituency Under Amrutha Nagarothana Grants-PKG-4**
Project Manager / Team Leader	:	**AARTN ASSOCIATES**
Project Start Date	:	**ARUN KUMAR DAS**
Project End Date	:	**03-09-2022**
Project Length in months	:	**02-09-2023**
	:	**12 MONTHS**

Sl. No.	Specifications	Unit	Schedule qty	Qty of work done	% of work done	Start date	End date	No. of working days	Remarks
1	Demolishing cement concrete manually/ by mechanical means including disposal of material to the appropriate disposal area as per direction of Engineer-in-charge. Nominal concrete 1:3:6 or richer mix (i/c equivalent design mix)	Cum	70.55	55.34	78	9-Sep-22	13-Sep-22	4	
34	Providing and laying in position Reinforced cement concrete for all Foundation works. The granite/trap/basalt crushed graded coarse aggregates and fine aggregates as per relevant IS Codes machine mixed with super plasticizers laid in finished layers, well compacted using needle vibrators, including all lead & lifts, cost of all materials, quality confirming to the requirements of relevant IS codes , labour, Usage charges of machinery, curing and all the other appurtenances required to complete the work as per technical specifications. (The cost of steel reinforcement & formwork to be paid separately) M25 Design Mix Using 20 mm nominal size graded crushed coarse aggregates (Including Centering and Shuttering for Columns) Qty Upto 125%	Cum	8.84	8.01	91	14-Sep-22	15-Sep-22	1	
35	Providing and laying in position Reinforced cement concrete for all Foundation orks. The granite/trap/basalt crushed graded coarse aggregates and fine aggregates as per relevant IS Codes machine mixed with super plasticizers laid in finished layers, well compacted using needle vibrators, including all lead & lifts, cost of all materials, quality confirming to the requirements of relevant IS codes , labour, Usage charges of machinery, curing and all the other appurtenances required to complete the work as per technical specifications. (The cost of steel reinforcement & formwork to be paid separately) M25 Design Mix Using 20 mm nominal size graded crushed coarse aggregates (Including Centering and Shuttering for Lintel, Beams, Slab) Qty Upto 125%	Cum	89.34	79.51	89	26-Sep-22	26-Sep-22	1	
36	Providing Thermo-Mechanically Treated bars of grade Fe-500D or more Steel reinforcement for R.C.C. work including straightening, cutting, bending, placing in position, binding and anchoring to adjacent members wherever necessary complete as per Design including cost of material, labour, usage charges complete as per specifications. (The laps and wastages shall not be measured separately) First Floor Qty Upto 125%	kg	13049.94	13049.94	100	23-Sep-22	25-Sep-22	2	
37	Providing and constructing load bearing wall with Solid Concrete blocks of size 400x150x200mm having block density more than 1800kg/m3 and minimum compressive strength of 4.00 N/mm2 conforming to IS 2185 (Part - I) - 2005 and constructed with CM 1:4 as per IS 2572:2005 including cost of all materials, labour, scaffolding and curing, usage charges of machinery etc complete as per specifications. First Floor	Sqm	253.80	229.52	90	3-Oct-22	13-Oct-22	10	
39	Providing 12 mm cement plaster with cement mortar 1:6 (1 cement: 6 fine sand) inclnding rounding off corners wherever required smooth rendering, providing and removing scaffolding, including cost of materials, labour, curing complete as per specifications and as per directions of Engineer-in-charge. First Floor Qty Upto 125%	Sqm	588.90	588.90	100	7-Nov-22	22-Nov-22	15	
44	Providing Honne wood frames of doors, windows, clerestory windows, ventilators and other frames, wrought, framed or assembled including making plaster groves (excluding cost of cement concrete and side clamps), but including cost of materials, labour, usage charges complete as per specifications First Floor Qty Upto 125%	cum	0.35	0.32	93	5-Nov-22	9-Nov-22	4	
47	Providing and fixing M.S. grills of required pattern in frames of windows etc. with M.S. flats, square or round bars etc. including priming coat with approved steel primer all complete. Fixed to openings / wooden frames with rawl plugs screws etc.	kg	2991.38	972.00	32	18-Nov-22	23-Nov-22	5	
51	Providing and laying in position Reinforced cement concrete for all Foundation works. The granite/trap/basalt crushed graded coarse aggregates and fine aggregates as per relevant IS Codes machine mixed with super plasticizers laid in finished layers, well compacted using needle vibrators, including all lead & lifts, cost of all materials, quality confirming to the requirements of relevant IS codes , labour, Usage charges of machinery, curing and all the other appurtenances required to complete the work as per technical specifications. (The cost of steel reinforcement & formwork to be paid separately) M25 Design Mix Using 20 mm nominal size graded crushed coarse aggregates (Including Centering and Shuttering for Columns)Qty Upto 125%	Cum	11.05	8.01	72	8-Nov-22	15-Nov-22	7	
52	Providing and laying in position Reinforced cement concrete for all Foundation works. The granite/trap/basalt crushed graded coarse aggregates and fine aggregates as per relevant IS Codes machine mixed with super plasticizers laid in finished layers, well compacted using needle vibrators, including all lead & lifts, cost of all materials, quality confirming to the requirements of relevant IS codes , labour, Usage charges of machinery, curing and all the other appurtenances required to complete the work as per technical specifications. (The cost of steel reinforcement & formwork to be paid separately) M25 Design Mix Using 20 mm nominal size graded crushed coarse aggregates (Including Centering and Shuttering for Lintel, Beams, Slab)Qty Upto 125%	Cum	89.55	78.38	88	23-Oct-22	30-Oct-22	7	

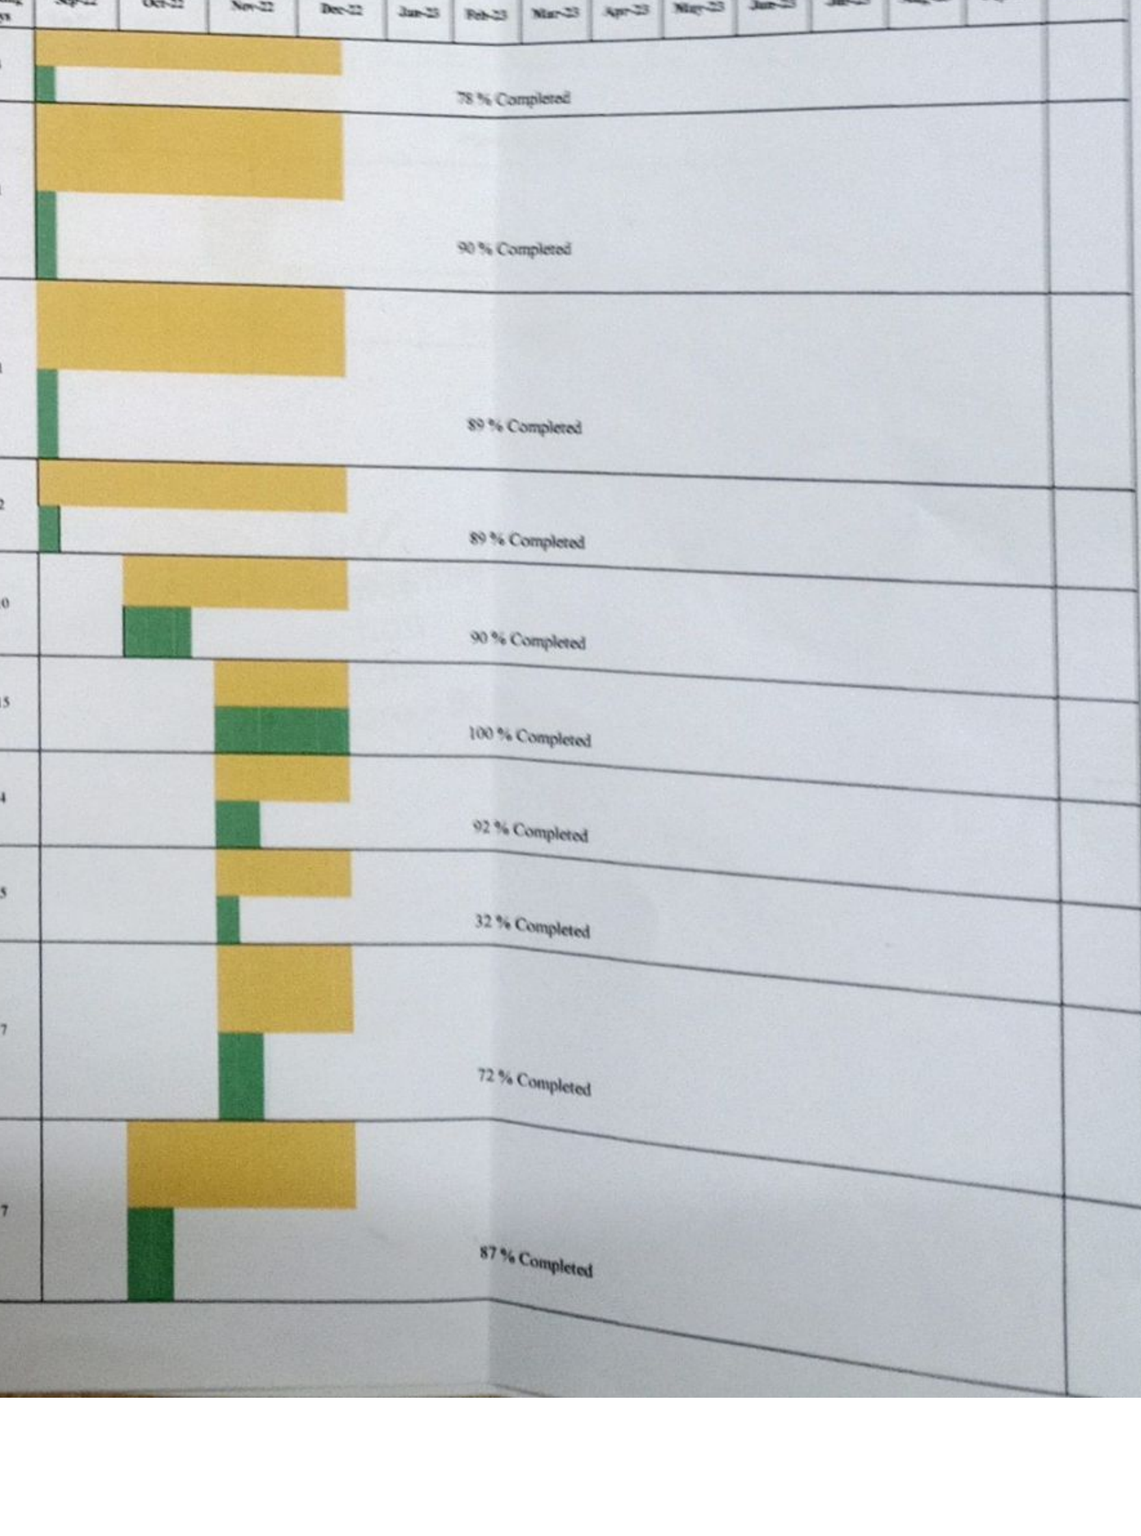

Scanned by TapScanner

BRUHAT BENGALURU MAHANAGARA PALIKE

Clients Name	:	EXECUTIVE ENGINEER YELAHANKA DIVISION
Project Name	:	Construction of Classrooms to Govt PU College and providing grill fencing and Other developmental Works to ISRO layout Park, Vishweshwarayya park, Raj kumar Park, Sri Saibaba park Yelahanka Assembly Constituency Under Amrutha Nagarothana Grants-PKG-4
Consultants	:	AARTN ASSOCIATES
Project Manager / Team Leader	:	ARUN KUMAR DAS
Project Start Date	:	03-09-2022
Project End Date	:	02-09-2023
Project Length in months	:	12 MONTHS

Sl. No.	Specifications	Unit	Schedule qty	Qty of work done	% of work done	Start date	End date	No. of working days	Sep-22	Oct-22	Nov-22	Dec-22	Jan-23	Feb-23	Mar-23	Apr-23	May-23	Jun-23	Jul-23	Aug-23	Sep-23	Remarks
53	Providing Thermo-Mechanically Treated bars of grade Fe-500D or more Steel reinforcement for R.C.C. work including straightening, cutting, bending, placing in position, binding and anchoring to adjacent members wherever necessary complete as per Design including cost of material, labour, usage charges complete as per specifications. (The laps and wastages shall not be measured separately) Second Floor	kg	13077.03	13077.03	100	20-Oct-22	25-Oct-22	5			100 % Completed											
54	Providing and constructing load bearing wall with Solid Concrete blocks of size 400x150x200mm having block density more than 1800kg/m3 and minimum compressive strength of 4.00 N/mm2 conforming to IS 2185 (Part - I) - 2005 and constructed with CM 1:4 as per IS 2572:2005 including cost of all materials, labour, scaffolding and curing, usage charges of machinery etc complete as per specifications. Second Floor	Sqm	252.45	228.07	90	4-Nov-22	20-Nov-22	16					90 % Completed									
64	Providing and fixing M.S. grills of required pattern in frames of windows etc. with M.S. flats, square or round bars etc. including priming coat with approved steel primer all complete. Fixed to openings / wooden frames with rawl plugs screws etc.	kg	2991.38	972.00	32	18-Nov-22	24-Nov-22	6					32 % Completed									

Legend → Planned %
→ Executed %

AARTN ASSOCIATES BANGALORE
DATE

Asst. Executive Engineer
Project Division
Yelahanka Zone
BBMP, Bangalore - 92

Scanned by TapScanner
